

Project EnergyConnect System Integration



Industry Update

February 2026




Transgrid



ProjectEnergyConnect.com.au

Purpose

- Project EnergyConnect (PEC) industry update
- Focus on System Integration activities
- Updates provided through [Project EnergyConnect website](#), as well as existing industry forums as appropriate

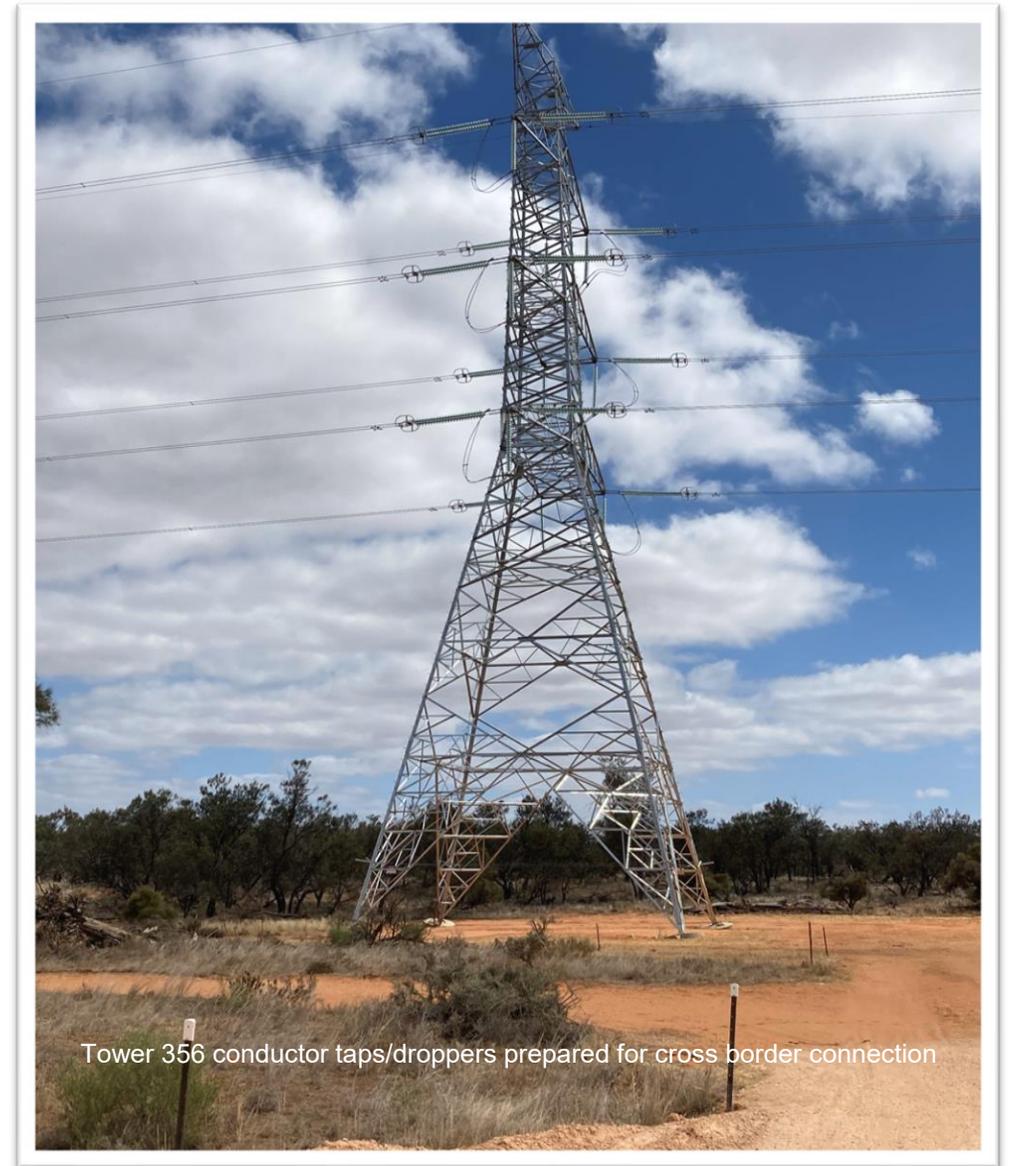

Outline

- High level status summary
- PEC key dates
- Inter-network testing
- Managing connection interest
- Overview of PEC-2 system integration activities
- Reference slides

High level status summary

Status summary

- Capacity across PEC will be released according to an agreed inter-network test program
- Inter-network tests can only start once the following pre-requisites have been met:

Pre-requisites	PEC-2 status
AEMO market systems are ready	On track
All network infrastructure is 'AEMO asset ready'	Expected end October 2026
Relevant Special Protection Schemes have been reviewed / commissioned	On track
Limits advice has been provided by TNSPs and developed into constraint equations by AEMO	On track

- Key milestones met:
 - PEC-1 capacity of +/- 150 MW released
 - PEC-2 limits updated for SA & NSW (refer slides 31 – 34 in this presentation)
- Key future milestones:
 - PEC-2 ready for inter-network testing – End Oct 2026



PEC key dates


PEC revised project schedule

- Construction continues to progress on the 700 km NSW section of PEC.
- The first stage of the project (PEC-1) is in service with 150 MW of capacity released in both directions.
- The second stage of the project will be completed and in service by the last quarter of 2026. Inter-network testing will then commence for release of up to 800 MW, subject to availability of suitable test conditions & successful test outcomes.
- Target dates for PEC-2 inter-network testing to start: End October 2026

Inter-network testing

PEC capacity release – key dates

Estimated dates and hold points for inter-network testing

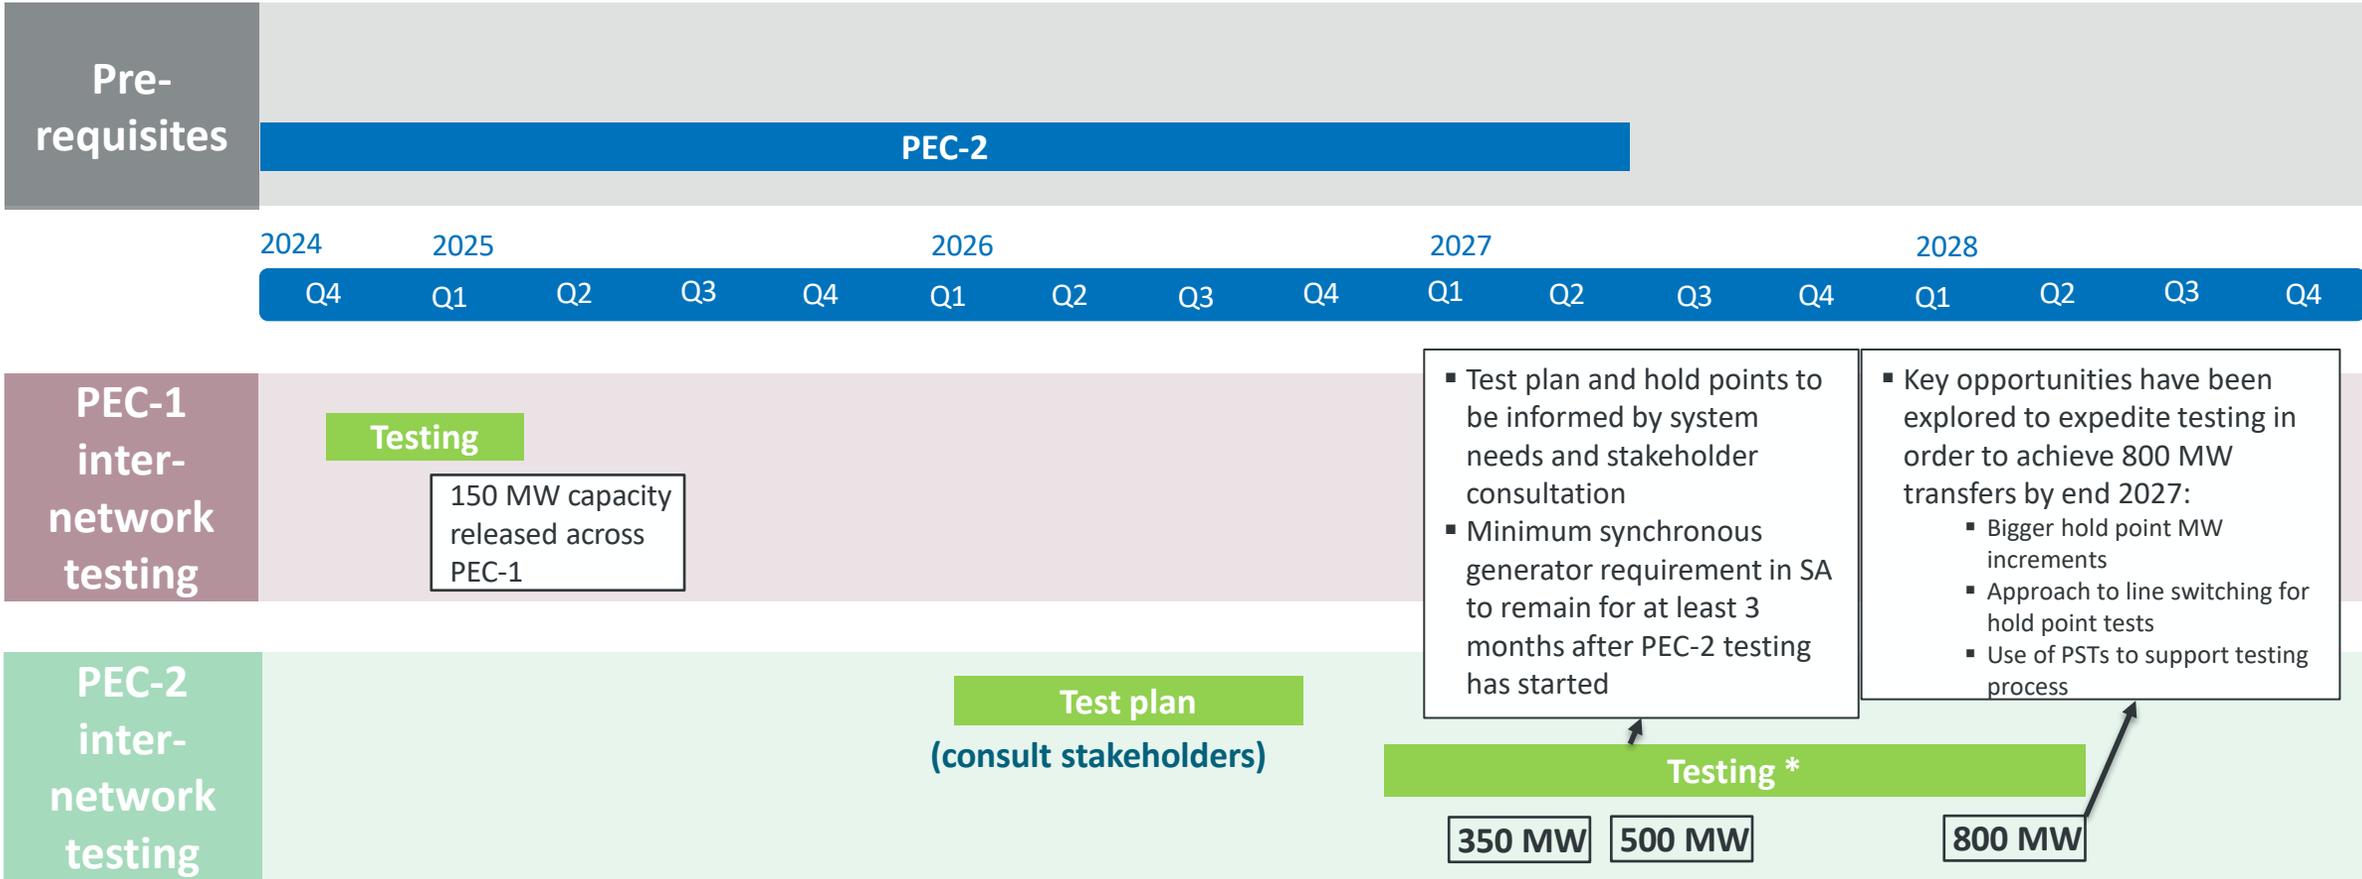

- Test plan and hold points to be informed by system needs and stakeholder consultation
- Minimum synchronous generator requirement in SA to remain for at least 3 months after PEC-2 testing has started


- Key opportunities have been explored to expedite testing in order to achieve 800 MW transfers by end 2027:
 - Bigger hold point MW increments
 - Approach to line switching for hold point tests
 - Use of PSTs to support testing process

* Subject to availability of suitable test conditions & successful test outcomes

Managing connection interest

Managing connection interest


- There is a staged approach to progressing connections to PEC. A connections framework outlining pre-requisites for each connection project phase relative to PEC milestones is [available on Project EnergyConnect website](#).
- A connections update was [published on the PEC website](#) in April 2024 when the Connection Application pre-requisites were met.
- Participants can request PEC modelling data via the AEMO data request page
- Connections to certain sections of PEC network infrastructure in NSW will be subject to South-West REZ access arrangements (for details see: <https://www.energyco.nsw.gov.au/sw-rez>)
- The key Connection Assessment Transition Framework consists of the following milestones:
 - Connection enquiry pre-requisites (Complete)
 - Connection application pre-requisites (Complete)
 - 5.3.4A/B approval pre-requisites
 - Registration and commissioning pre-requisites



Draft connection assessment transition framework

Milestones	Connection Enquiry pre-requisites	Connection Application pre-requisites	5.3.4A/B approval pre-requisites	Registration and Commissioning pre-requisites
Status	Achieved in March 2023	Achieved in March 2024	In Progress	
PEC milestone	<ul style="list-style-type: none"> PEC formally achieves Considered status 	<ul style="list-style-type: none"> PEC detailed design complete (design data available including functional requirements of South Australia Intertrip Remedial Action Scheme (SAIT RAS)) 	<ul style="list-style-type: none"> Detailed design of SAIT RAS finalised and complete 	<ul style="list-style-type: none"> SAITRAS commissioned and in service (including impact assessment on Heywood Interconnector) PEC internetwork testing completed, and 500 MW transfer capacity released across PEC
PEC model maturity	<ul style="list-style-type: none"> PEC planning models (PSS/E) available via AEMO data request PEC PowerFactory model available 	<ul style="list-style-type: none"> Standard or Detailed (S/D) data for Buronga and Dinawan synchronous condensers (syncons) available 	<ul style="list-style-type: none"> PEC R1 dynamic models (PSS/E and PSCAD) available (including Buronga and Dinawan syncons) 	<ul style="list-style-type: none"> PEC R2 dynamic models (PSS/E and PSCAD) available (including Buronga and Dinawan syncons)
PEC limit advice, Special Protection Schemes (SPS) and other considerations	<ul style="list-style-type: none"> Preliminary PEC Limit advice available 	<ul style="list-style-type: none"> Preliminary PEC limit advice available Preliminary limit advice available for nearby key transmission lines For connections to the NSW end of PEC, updated NSW SPS details (including preliminary impact on existing SPS in NSW) SAIT RAS functional requirements available 	<ul style="list-style-type: none"> AEMO PEC constraint equations available. AEMO constraint equations available for nearby key transmission lines For connections to the NSW end of PEC, updated NSW SPS details (including impact on existing SPS in NSW) SAIT RAS impact assessment and coordination of any new control schemes by newly proposed connecting plant completed 	<ul style="list-style-type: none"> AEMO constraint equations for PEC and nearby key transmission lines available and active SAIT RAS, NSW SPS details and limit advice updated based on connecting plant impacts

Proposed connection process after NSW South West REZ Declaration

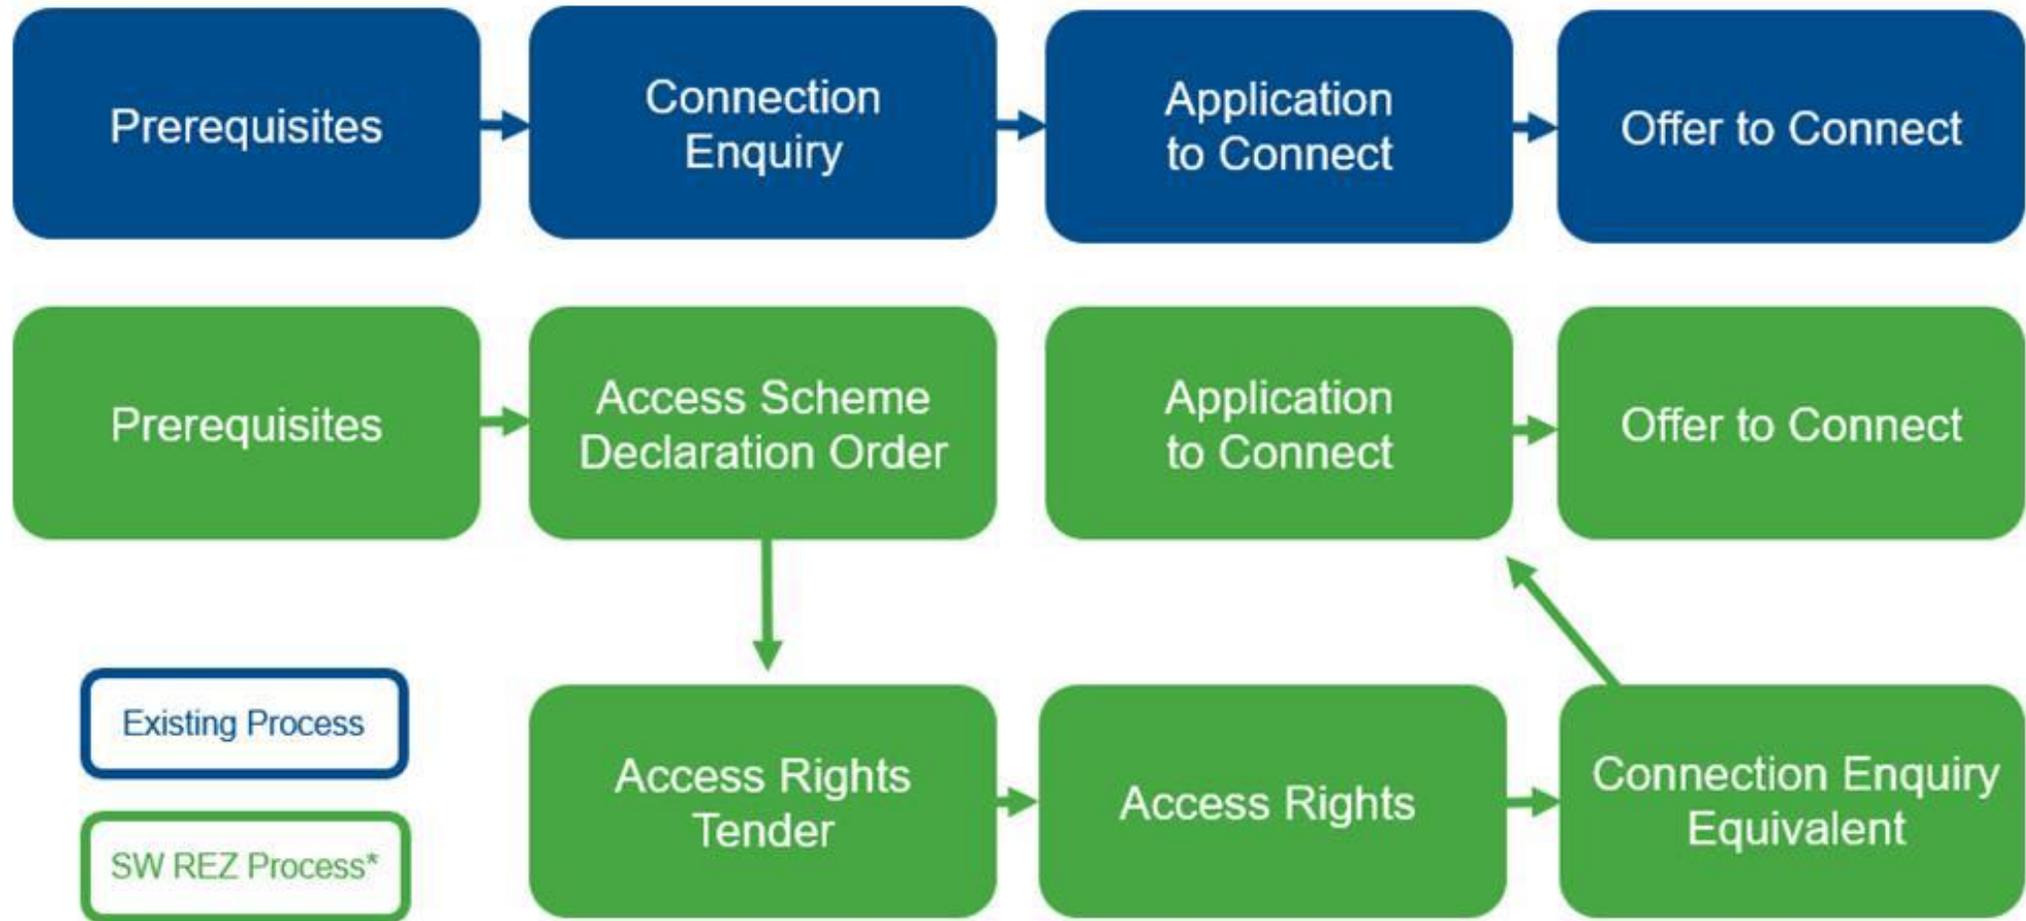

* SW REZ process applies only for projects seeking connection to SW REZ 'access rights network'

Overview of PEC-2 system integration activities

Overview of PEC-2 system integration activities

- Market integration activities:
 - [Rule change proposal](#) pending with AEMC
- Develop range of system limits
- Review of existing special protection schemes
- Developing the South Australian Interconnector Trip Remedial Action Scheme (SAIT RAS) to prevent SA being separated from the NEM for the non-credible loss of either PEC or the Heywood interconnector corridors
- Explored opportunities to expedite PEC-2 inter-network testing
- Connection applications that impact on the PEC corridor will have to be carefully considered taking the above integration activities into account



Thank You!



System Integration Steering Committee:

Hugo Klingenberg, ElectraNet

Kasia Kulbacka, Transgrid

Teresa Smit, AEMO

Ashley Lloyd, VicGrid



Transgrid



ProjectEnergyConnect.com.au



Reference Slides



Transgrid



ProjectEnergyConnect.com.au

Governance of System Integration activities

- System Integration Steering Committee (SISC) has responsibility for system integration activities, including stakeholder engagement as required
- The SISC is overseen by an Executive SISC comprising relevant ElectraNet, AEMO, Transgrid and VicGrid Executives and Project Directors

Key objectives of PEC System Integration Steering Committee

- Collaboration across AEMO, ElectraNet, Transgrid and VicGrid to coordinate timely PEC integration into the National Electricity Market (NEM)
- Provide governance and reporting in accordance with National Electricity Rules (NER) frameworks and meet all requirements of clause 5.7.7 of the NER
- Achieve combined transfer limit across both the Heywood and PEC interconnectors of 1,300 MW import into South Australia and 1,450 MW export. The project is designed to achieve these transfer levels with consideration of non-credible loss of either interconnector


Project EnergyConnect

- PEC is a geographically diverse second Alternating Current (AC) interconnector that will significantly increase the transfer capability between South Australia and the rest of the National Electricity Market
- This will increase access to other regions and increase competition in the wholesale electricity market putting downward pressure on electricity prices

Interconnector	Nominal Limit (MW)	Nominal Combined Limit (MW)	Combined Transfer Limit ¹
Heywood Interconnector (HIC)	+/- ² 650	+/- 1450	+ 1300
Project EnergyConnect (PEC)	+/- 800		- 1450

1. Combined transfer limit dependent on transient system stability and sufficient loads and generators in the SAIT RAS
2. + import into SA
- export from SA
3. Current transfer limit is SA-VIC: 700 MW, VIC-SA: 750 MW
4. Transmission augmentation information: <https://aemo.com.au/en/energy-systems/electricity/national-electricity-market-nem/nem-forecasting-and-planning/forecasting-and-planning-data/transmission-augmentation-information>

Scope - PEC stage 1 (PEC-1)

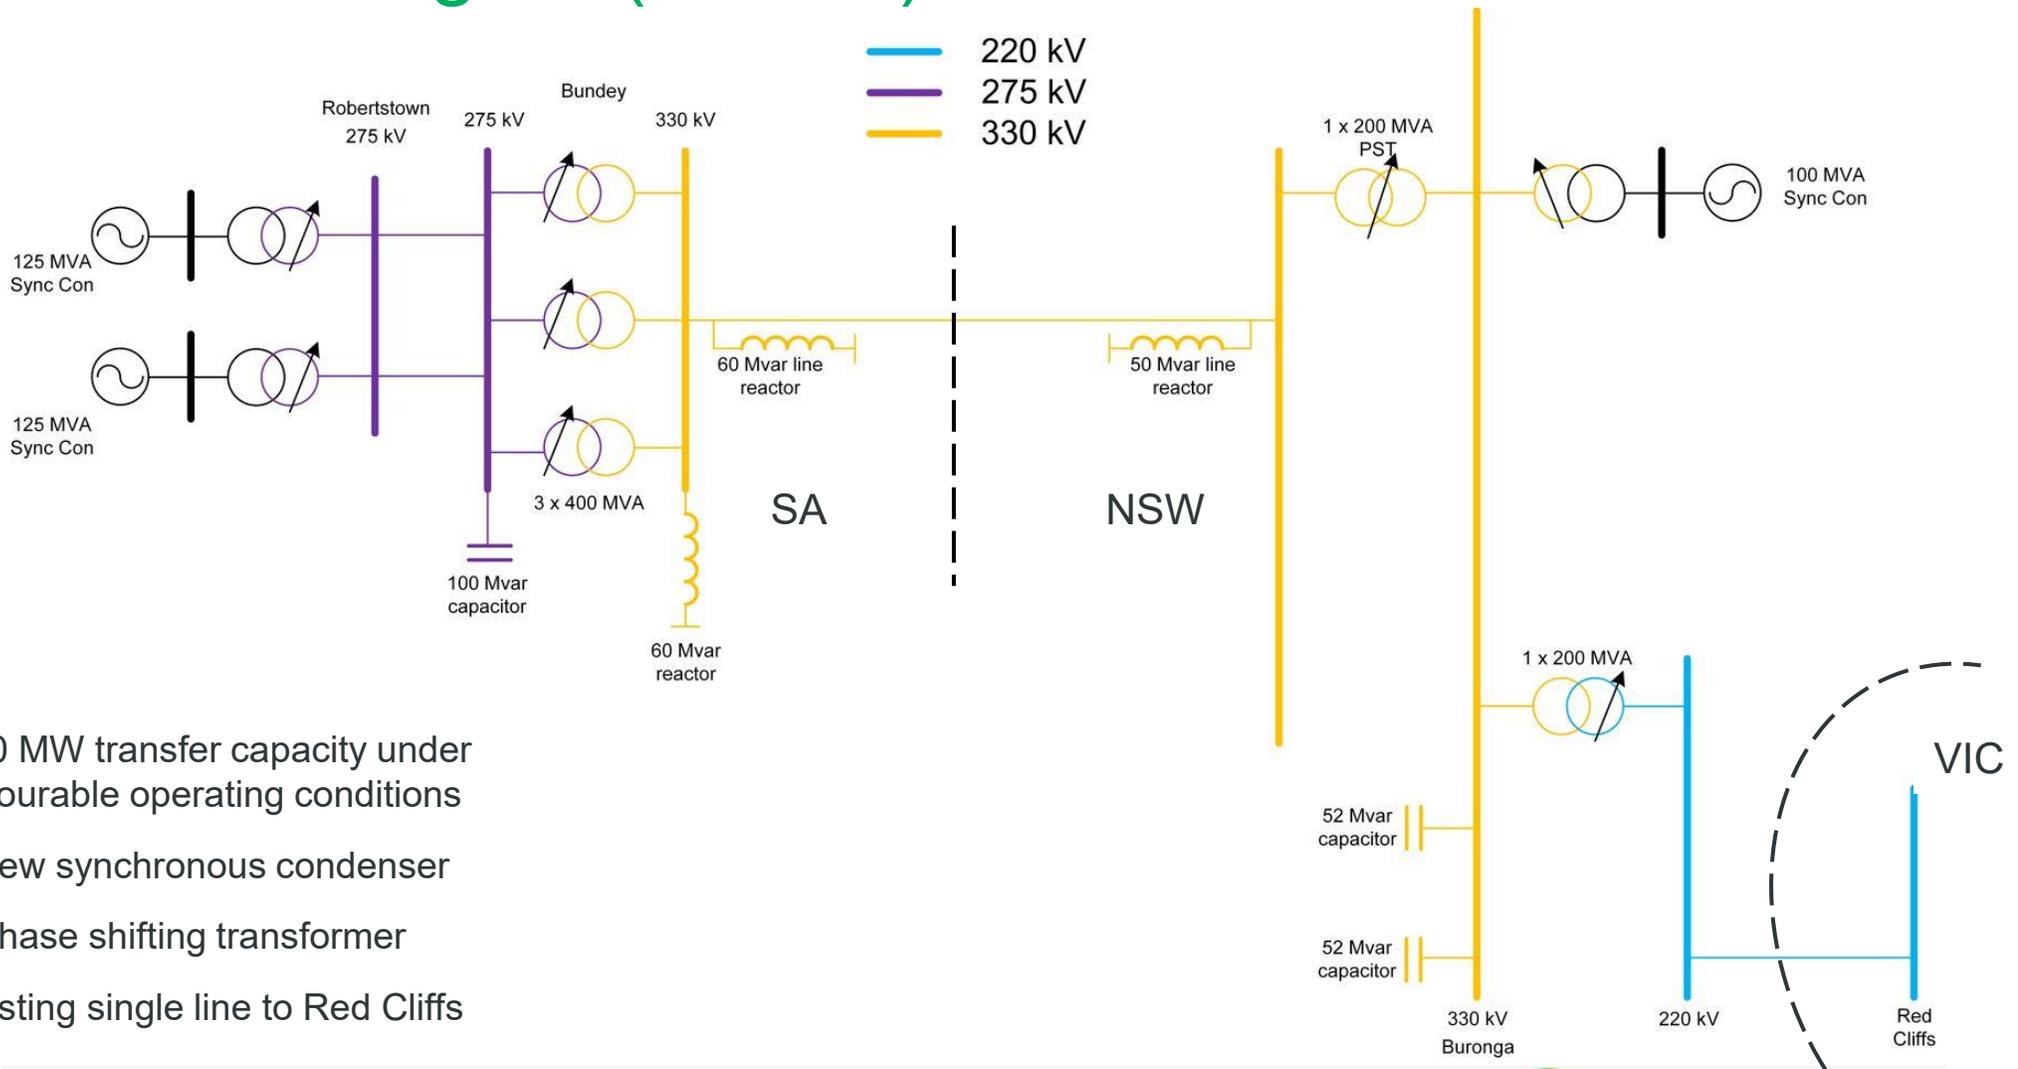

- 150 MW transfer capacity under favourable operating conditions
- 1 new synchronous condenser
- 1 phase shifting transformer
- Existing single line to Red Cliffs

Key changes – PEC-1

PEC-1 results in effectively a bigger Heywood Interconnector (HIC)

Vast majority of existing constraints are expected to remain in place

- HIC trip will intertrip PEC-1
- PEC-1 150 MW – in both directions (with slight reduction at very high Murraylink flows)
- Combined transfer limits for PEC-1 and HIC - SA-VIC: 700 MW, VIC-SA: 750 MW*

Impact on existing Special Protection Schemes (SPSs):

- All Special Protection Schemes (SPSs) potentially impacted by the PEC-1 integration have been reviewed – One change: Trip parallel 132 kV circuit for either Tailem Bend to South East or Tungkillo to Tailem Bend 275 kV line trips
- Murraylink Very Fast Run Back (VFRB) scheme has been upgraded

*Additional HIC capacity release is subject to effective management of interconnector drift and consideration of impact of mainland contingencies on SA interconnector flows.

PEC-1 Inter-network testing

Summary of planned testing under NER 5.7.7:

- Three hold points with PEC-1 in service
- Tests include:
 - PST tapping test (at initial hold point)
 - South East – Tailem Bend or Robertstown – Tungkillo 275 kV switching
 - Buronga – Bundey 330 kV line switching
 - Murraylink interconnector reactive power step change or Buronga synchronous condenser voltage step change
 - Generic system damping assessment

Timeline:

- Industry consultation – Complete
- Final [inter-network test plan](#) – Published
- Commence inter-network testing – Complete
- Complete PEC-1 inter-network testing – Complete
- HIC inter-network testing – In progress

Impact of constraint changes – PEC-1

PEC-1 constraint / limit changes

New constraints

- Overload on Buronga PST for trips of Murraylink


Revised limits

- Existing Line X5 (Balranald – Darlington Point) voltage stability limit
- Existing thermal limits in NW Vic and SW NSW to include PEC term
- System strength limits under outages in NW Vic
- Further revision to limit factors (due to second Buronga – Red Cliffs 220 kV circuit)

Revocation of the existing SA protected event

- As discussed in a previous industry update, the Reliability Panel published its final determination on AEMO's request on 14 September 2023.
- The SA protected event was revoked on 30 March 2024 in advance of the expected synchronisation and testing of PEC Stage 1.
- Constraints associated with destructive wind conditions are now according to the Power System Security Guidelines (Operational Procedure 3715).
- AEMO will review the limits to apply during destructive wind conditions post PEC-2.

Scope - PEC stage 2 (PEC-2)

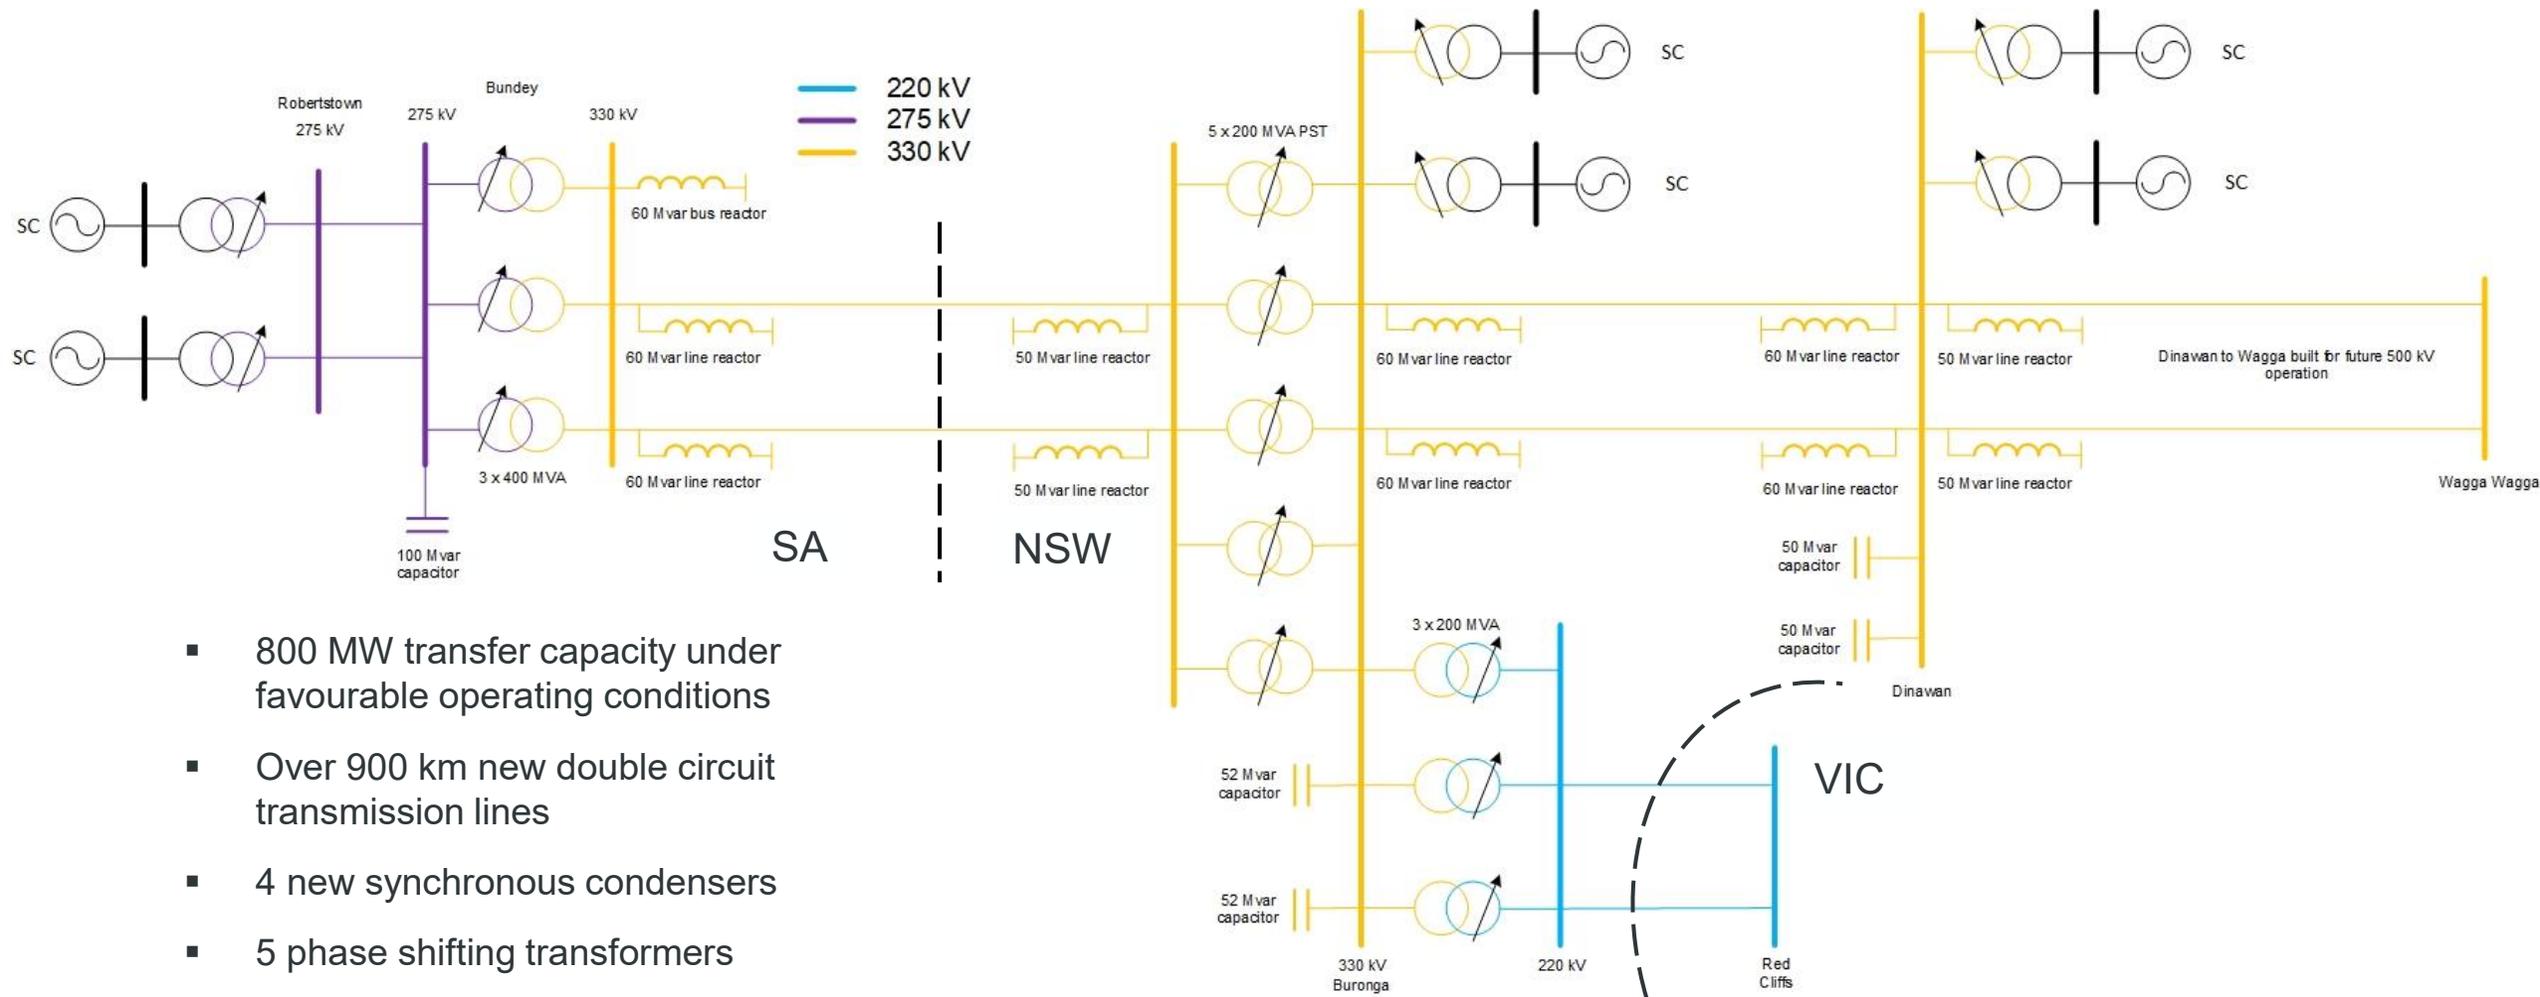


- 800 MW transfer capacity under favourable operating conditions
- Over 900 km new double circuit transmission lines
- 4 new synchronous condensers
- 5 phase shifting transformers


Phase Shifting Transformers (PSTs): Expected operation

- PST allows balancing of power flow sharing across the PEC and Heywood (HIC) Interconnectors
- Taps can be manually or automatically changed to divert flows between HIC and PEC when one of them gets closer to limits
- At times of high transfer, each PST tap change is expected to vary PEC flow by about 10 MW with PEC-1, and about 20 MW with PEC-2

Example	PST tap angle (degrees)	HIC (MW)	PEC (MW)	Combined transfer (MW)
SA import	17	670	630	1300
	20	650	650	1300
	40	510	780	1290
	0	780	520	1300
SA export	-25	730	710	1450
	-28	710	730	1450
	-40	640	810	1450
	0	890	530	1420

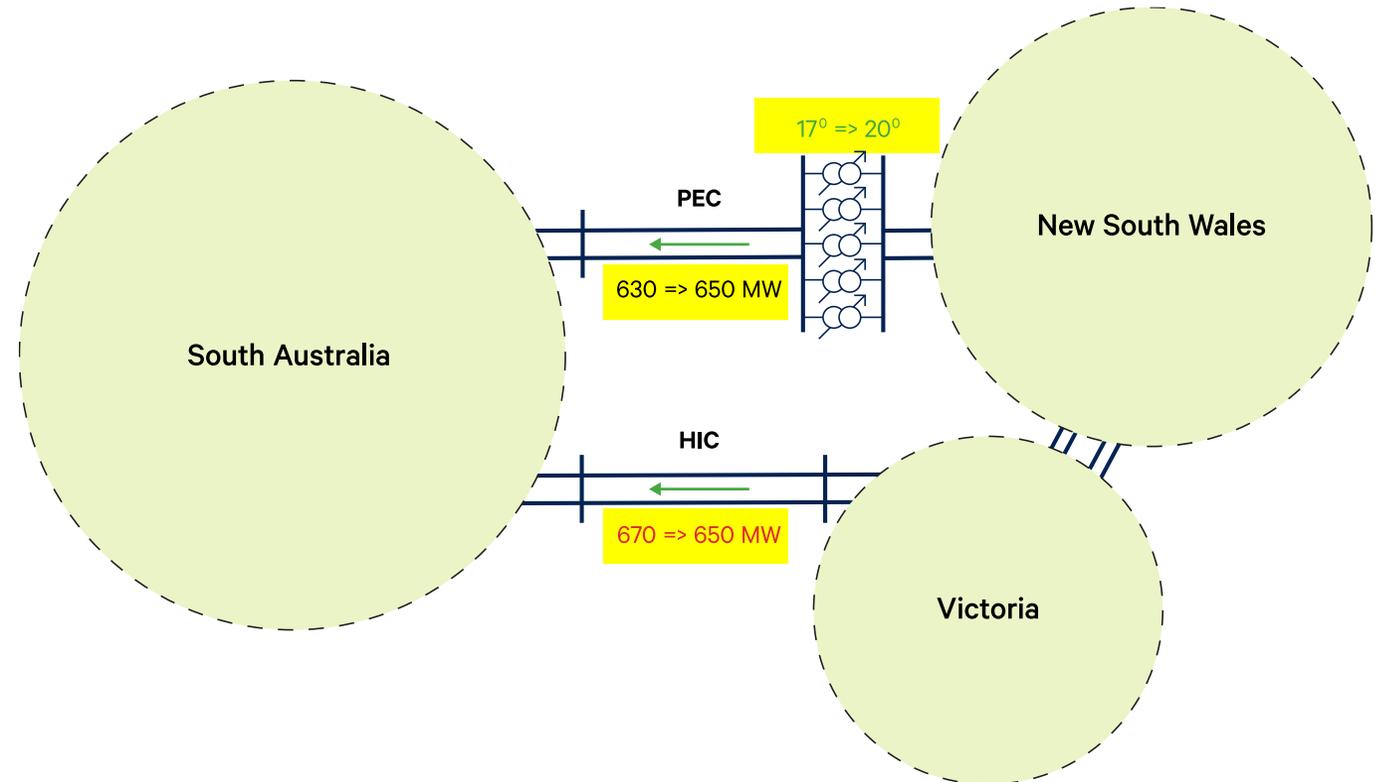

Phase Shifting Transformers (PSTs): Control Strategy Overview

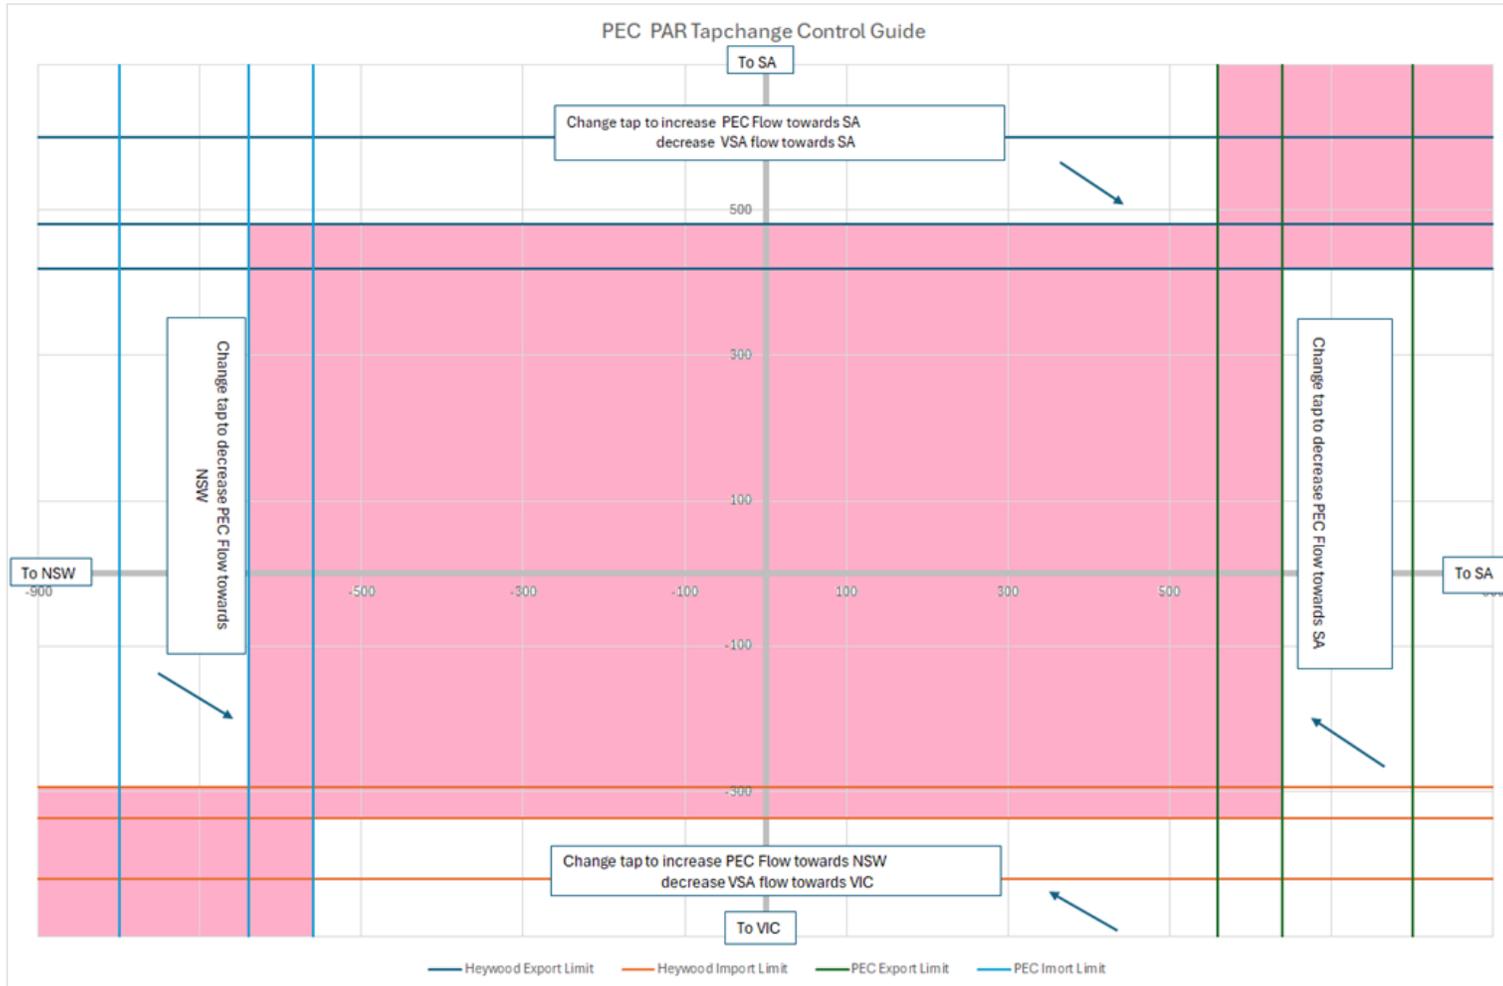

- System normal conditions: PSTs operated in Auto mode to enable automated power flow balancing across the HIC and PEC interconnectors
- Auto mode: PST tap changer will operate when one interconnector is above 80% of its telemetered limit, while the other is below 70% of its telemetered limit (white areas in the figure)
- The tap changer will not operate when the interconnectors are not approaching constraints or are equally constrained (pink areas in the figure).
- Non-Auto control mode will be activated under abnormal or high-risk system conditions. Under Non-Auto mode, the PSTs will be manually controlled by Transgrid under AEMO's instruction.
- PEC and Heywood Interconnector limits are expected to be telemetered from AEMO's dispatch engine via ICCP link to Transgrid's SCADA for implementation.

AEMO's PEC market integration - dispatch

- Revise existing [automated Negative Residue Management \(NRM\)](#)
 - To ensure benefits flow to consumers from constructing and energising transmission loops and related transmission infrastructure, AEMO will not 'clamp' looped interconnectors to limit negative IRSR when 'net' loop IRSR is positive. Additionally, clamping would reduce the overall benefits of PEC by restricting the flow of electricity over the interconnector until negative IRSR is below the predefined threshold set by AEMO.
 - AEMO will introduce logic that permits the accumulation of negative IRSR on the VicSA, SA-Vic, SA-NSW, NSW-SA, NSW-Vic and Vic-NSW directional interconnectors while the net total of these residues ('loop-aggregate residue') remains positive. To implement this, a new Loop NRM Flag field will record the status of this aggregate residue, with a value of either 0 or 1. This change will occur in August 2026.
- Revise existing price-scaling algorithm to include a transmission loop. This change will occur in August 2026.
- PEC Stage 2 will be registered as a separate interconnector (NSW1-SA1). VNI and VIC-SA will revert to pre-PEC Stage 1 state.

More information:

- [AEMO Consultation on Automation of Negative Residue Management for the implementation of transmission loops](#)
- [AEMO Project Market Connect – Market Integration Project](#)

AEMO's PEC market integration - Settlements

AEMC published its final determination on the [inter-regional settlements residue arrangements for transmission loops \(IRSR rule\)](#) on 25 September 2025, and it commenced on 2 October 2025.

PEC will be a nominal 800 MW bidirectional interconnector between South Australia and New South Wales, with an additional connection to Victoria. This will require IRSR to be allocated across three sets of directional interconnectors, with the IRSR rule providing for a 'net trade' approach to allocation.

The IRSR rule includes transitional provisions (NER 11.188) for the:

- 'Loop operations start date', when PEC is represented as a separate directional interconnector in AEMO's dispatch systems (must occur between on 1 October and 2 November 2026).
- 'Loop settlements start date', when AEMO's settlement system is updated to allow settlements to occur for looped interconnectors under the new arrangements) (must occur between the 'loop operations start date' and 2 November 2026).

More information:

- [AEMC Inter-regional settlements residue arrangements for transmission loops](#)
- [AEMO Project Market Connect – Market Integration Project](#)

AEMO's PEC market integration - Settlements (cont)

- AEMO's current plan is to:
 - Represent the PEC loop in AEMO's dispatch systems from 1 October 2026.
 - Commence new IRSR calculations on 1 November 2026 (start of settlement week) – this is anticipated to be the earliest feasible system implementation for the settlements methodology change.
- Under the IRSR rule, AEMO must also:
 - Use reasonable endeavours to establish new unit categories for PEC and conduct at least one auction of those units before October 2026 (starting from Q4 2026).
 - Review and amend the SRA Rules as necessary or appropriate to take account of the IRSR rule, before the earlier of four weeks prior to the loop operations start date and 10 business days prior to the first auction of PEC unit categories.

More information:

- [Consultation on Settlements Residue Auction Rules - EnergyConnect](#)
- [AEMO Project Market Connect – Market Integration Project](#)

Anticipated constraints for PEC-2

New constraints:

- Physical design limits result in a combined system normal limit of 1,300 MW import into SA and 1,450 MW export from SA across PEC and HIC, e.g. Buronga PST range. However, due to voltage and transient stability, this combined limit is dependent on the total underlying system demand and DER generation levels in SA. Study results indicate that, under system normal operating conditions (without any synchronous generator online in SA), underlying system demand must be less than 3800 MW for SA import conditions and less than 4000 MW for SA export conditions to achieve the combined SA import of 1300 MW and combined SA export of 1450 MW respectively
- ElectraNet and Transgrid have developed voltage stability and transient stability limits based on the PEC-2 network configuration, demand and DER levels for system normal and key N-1 network operating conditions

Constraints being revised:

- Expecting thermal limits in NW Vic and SW NSW to include PEC-2
- System strength limits assessed with PEC-2 and HIC operating in parallel
- System oscillatory (damping) limits assessed with PEC-2 and HIC operating in parallel

Anticipated conditions where above combined transfers may not be fully achievable:

- Network element outages – refer next slides
- Regional generation dispatch or availability of generation sources
- Impact of local demand close to the PEC & HIC corridors

Expected impact of prior outages following PEC-2 (1/3)

The MW values quoted are based on limited studies and are indicative only

Prior Outage	Expected impact on transfer capability	Expected impact on generators (in addition to transfer capability, mainly system strength)	Comment
Any circuit along the Wagga-Buronga-Bundey-South East-Heywood-Moorabool corridor (PEC and HIC corridor)	An outage of one circuit on this corridor results in additional limits to cater for the loss of the other circuit which is a credible contingency event. Combined transfers across PEC and HIC will be reduced to between 900 - 1050 MW depending on the outage elements	SA: No system strength impact NSW: No pre-contingent disconnection of existing renewable generators in south west NSW VIC: No impact on Vic gens anticipated	
SA transmission line (not on the PEC and HIC corridor)	Minimal impact expected on PEC and HIC transfers. Existing voltage limits are present in the Mid North of SA for outages on the Robertstown to Davenport corridor	SA: Local impact only, effectively the same as current limits NSW & VIC: Minimal impact expected	
NW Victoria transmission line (not on PEC and HIC corridor)	Minimal impact on PEC	VIC: Some impact depending on location / anti-islanding schemes SA & NSW: Minimal impact expected	
Any one SVC in South Australia	Expected to be less than 50 MW reduction	SA: No system strength impact NSW: No pre-contingent disconnection of existing renewable generators in south west VIC: No impact on Vic gens anticipated	
Any one synchronous condenser at Davenport or Robertstown	Expected to be less than 50 MW reduction	SA: SA instantaneous IBR generation limit of 3,000 MW NSW & VIC: Minimal impact expected	

3:

Expected impact of prior outages following PEC-2 (2/3)

The MW values quoted are based on limited studies and are indicative only

Prior Outage	Expected impact on transfer capability	Expected impact on generators (in addition to transfer capability, mainly system strength)	Comment
Any one synchronous condenser at Buronga or Dinawan	About 50 MW reduction	SA: Minimal impact expected NSW: No pre-contingent disconnection of existing renewable generators in south west NSW VIC: No impact on Vic gens anticipated	
Buronga to Red Cliffs Line X1	Expected to be less than 50 MW reduction	Balranald renewable generation can remain in service; Broken Hill renewable generation can remain in service	Line X1 trip scheme modified
Buronga to Balranald Line X3	Expected to be less than 50 MW reduction	Balranald 220 kV renewable generation to be disconnected as per existing arrangements; Broken Hill renewable generation can remain in service	Line X3 trip scheme to be modified
Balranald to Darlington Point Line X5	About 50 – 100 MW reduction	Balranald renewable generation can remain in service; Broken Hill renewable generation can remain in service	Line X5 trip scheme to be modified

Expected impact of prior outages following PEC-2 (3/3)

The MW values quoted are based on limited studies and are indicative only

Prior Outage	Expected impact on transfer capability	Expected impact on generators (in addition to transfer capability, mainly system strength)	Comment
Darlington Point to Wagga Line 63	Expected to be less than 50 MW reduction	Darlington Point renewable generation to be disconnected as per existing arrangements; Balranald renewable generation can remain in service; Broken Hill renewable generation can remain in service; Line X5 to be opened as per existing arrangements	Line 63 trip scheme to be modified
Lower Tumut to Wagga Line O51; or Wagga to Jindera Line 62; or Jindera to Wodonga Line O60; or Dederang to Wodonga 330 kV Line	PEC 330 kV may need to be opened at Wagga depending on south west NSW load and generation; PEC transfers could be limited to less than 100 - 200 MW at these times	Renewable generation in Wagga – Darlington Point area to be disconnected; Balranald and Broken Hill renewable generation can remain in service	Humelink will resolve

Anticipated construction outages


- All previously scheduled construction outages have been successfully completed.
- Transgrid continues to work with its delivery partner to explore opportunities to minimise future construction outages on PEC.

PEC-2 – Managing non-credible events

- Electricity transmission networks are designed and operated to withstand credible contingencies
- It would be prohibitively expensive to design and build a transmission system that can withstand non-credible contingencies without impacting on loads and/ or generators
- Instead, Emergency Control Schemes are used to keep the system connected and stable if non-credible contingencies happen
- The South Australian Interconnector Trip Remedial Action Scheme (SAIT RAS) is being developed to prevent SA being separated from the NEM
- Other RASs may be required to cater for non-credible events ‘out of scope’ for SAIT RAS, e.g.
 - Non-credible loss of the Buronga – Red Cliffs 220 kV lines
 - Non-credible loss of Moorabool - Sydenham 500 kV lines with significant generation connecting on that corridor
 - Non-credible loss of Buronga – Dinawan – Wagga 330 kV lines if significant generation connects on that corridor
- Number of impacted RASs being reviewed
 - SA: 7 ; NSW: 7 ; VIC: 4

SAIT RAS

Concept design

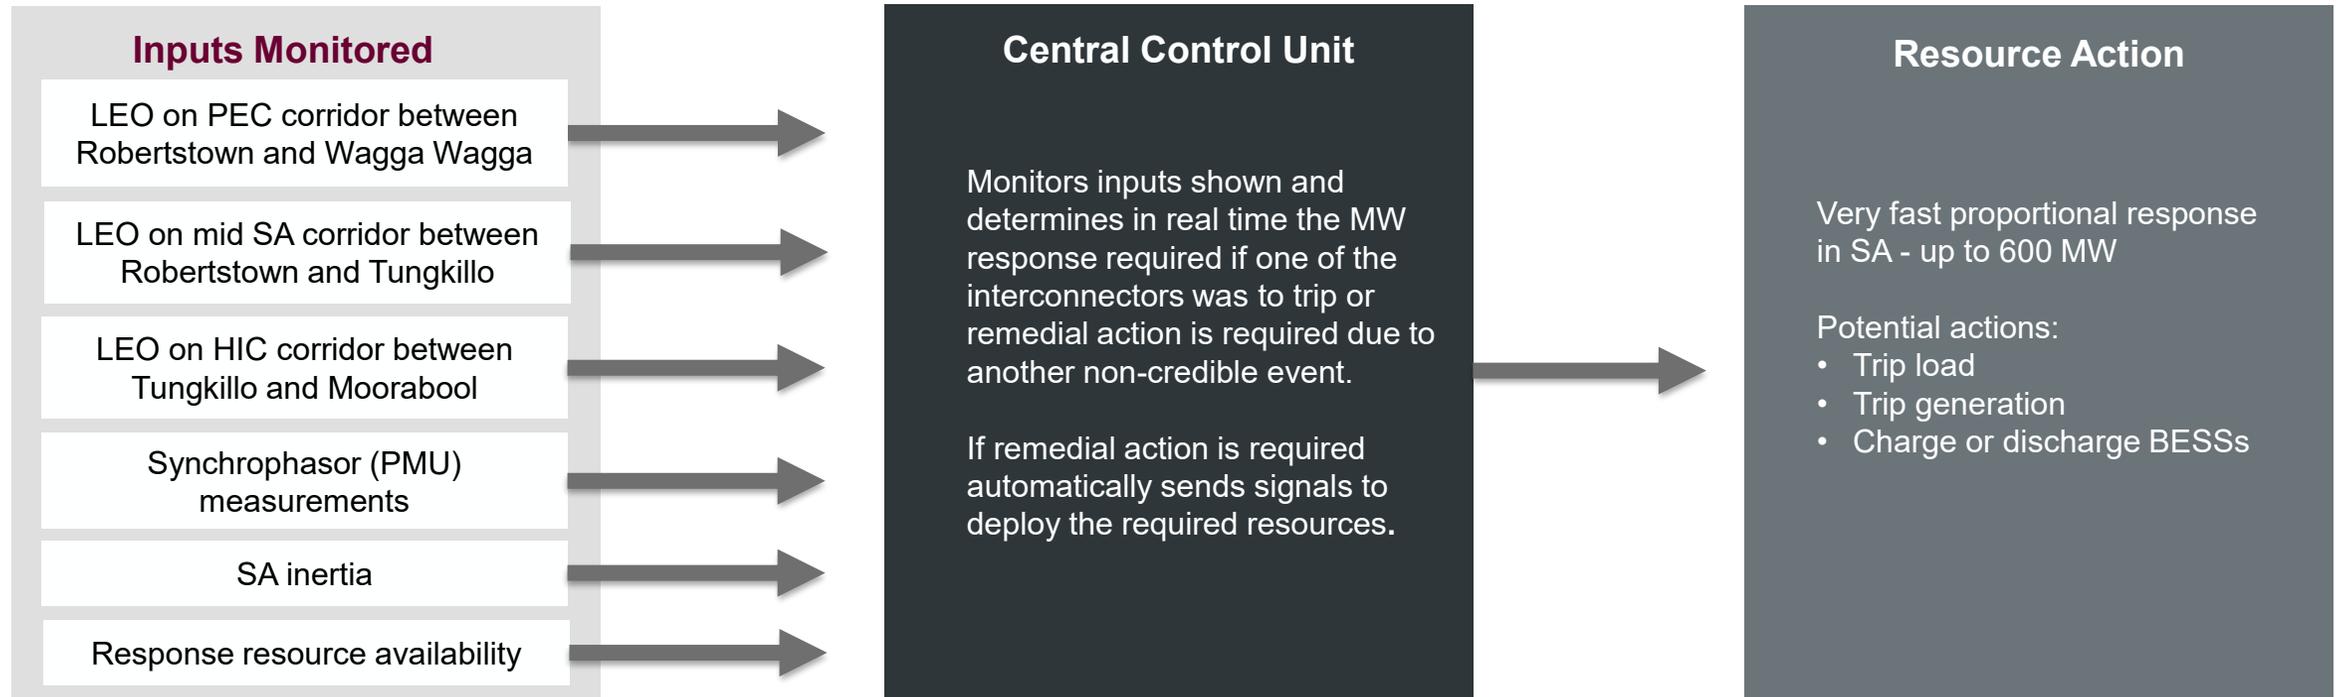

Duplicated high-speed communications into Victoria and NSW

Duplicated high-speed communications to resource response sites

Telecommunications requirements

SA– South Australia **LEO**– Line End Open **PEC**– Project EnergyConnect **HIC**– Heywood Interconnector **BESS**– Battery Energy Storage System
